

Filing Receipt

Received - 2023-02-13 10:15:53 AM Control Number - 52667 ItemNumber - 119

PROJECT NO. 52667

FILING OF ATTESTATIONS	§	PUBLIC UTILITY COMMISSION
DEMONSTRATING COMPLIANCE	§	
WITH HB 4150	§	OF TEXAS

TWELFTH PROGRESS REPORT OF DENTON COUNTY ELECTRIC COOPERATIVE, INC., D/B/A COSERV ELECTRIC

Denton County Electric Cooperative, Inc. d/b/a CoServ Electric files this progress report regarding compliance with Section 6 of House Bill 4150 ("HB 4150"), providing information regarding distribution lines on United States Army Corps of Engineers ("USACE") property that CoServ Electric identified as non-compliant in its report and attestation filed in this docket on January 14, 2022 ("Initial Report"). By letter dated March 4, 2022, the Division of Compliance and Enforcement ("DICE") of the Public Utility Commission of Texas ("Commission") requested a progress report and additional information to be filed on a monthly basis. This is CoServ Electric's twelfth monthly progress report, which is timely filed.

I. Twelfth Progress Report

In its last progress report, CoServ Electric identified four distribution line segments located in areas that could be suitable for a sailboat and remained non-compliant with the applicable clearance standards in Rule 232 of NESC Standard ANSI (c)(2) ("NESC Rule 232"). These four line segments remain in progress at Lake Ray Roberts or Lake Lewisville, as described below. Availability of atypical, taller poles continues to delay completion of construction for three of these line segments. Fortunately, CoServ Electric has received all materials to complete the Ray Roberts 20 project, and estimates construction for that project will be completed in two to three weeks.

1. Status of engineering design, permitting, and reconstruction.

The status of the four remaining distribution line segments is as follows:

- Ray Roberts 3 In construction; waiting for further delivery of 75-foot and 80-foot wood poles.
- Ray Roberts 20 In construction; all materials received; estimated completion in two to three weeks.

- Lewisville 31A Electrician and customer still working with USACE to install new
 customer-owned meter pedestal and underground facilities to four existing boathouses
 and one security light. Once the pedestal is located, CoServ Electric design will be
 finalized and released to construction. CoServ Electric will remove all existing
 overhead facilities from USACE property after completion of underground service
 installation.
- Lewisville 34 Permit approved; waiting for delivery of 90-foot concrete pole to begin construction.

Further information is provided in Attachments A and B attached hereto.

Date: February 13, 2023 Respectfully submitted,

Carl R. Galant

State Bar No. 24050633

Travis Vickery

State Bar No. 00794790

1111 W. 6th Street, Bldg. B, Suite 400

CIR. CQ


Austin, Texas 78703


Phone: (512) 495-6083 Fax: (512) 505-6383

 $\underline{cgalant@mcginnislaw.com}$

tvickery@mcginnislaw.com

ATTORNEYS FOR COSERV ELECTRIC

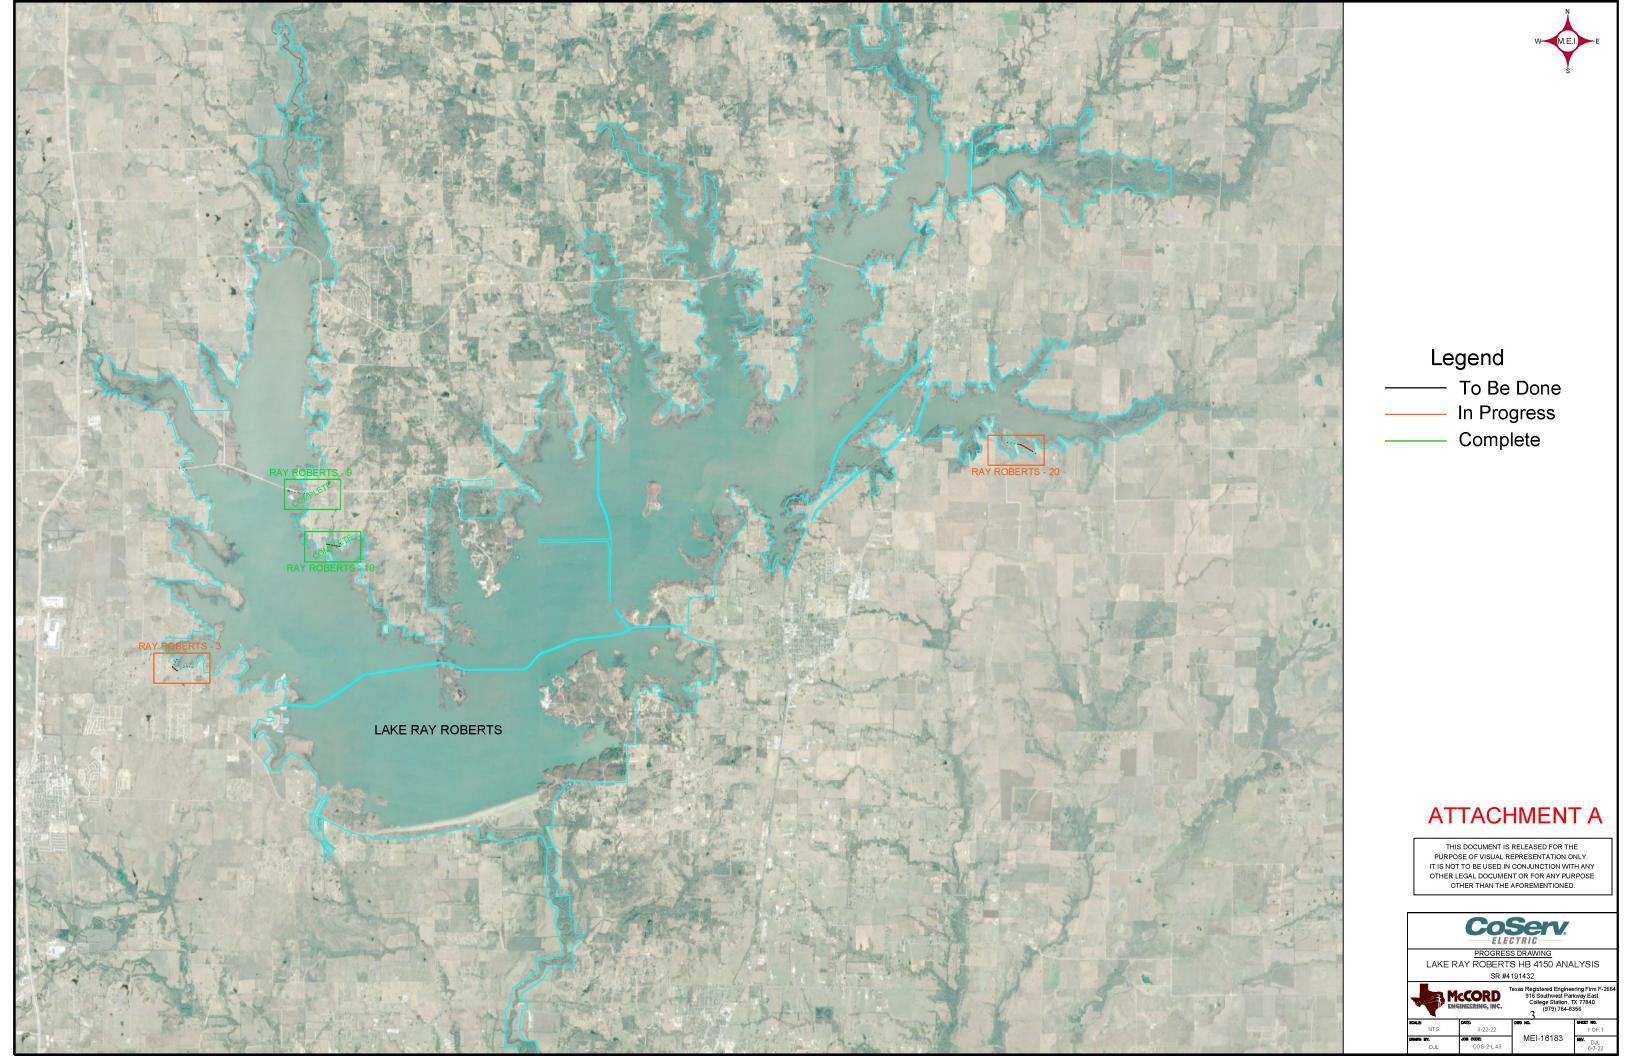

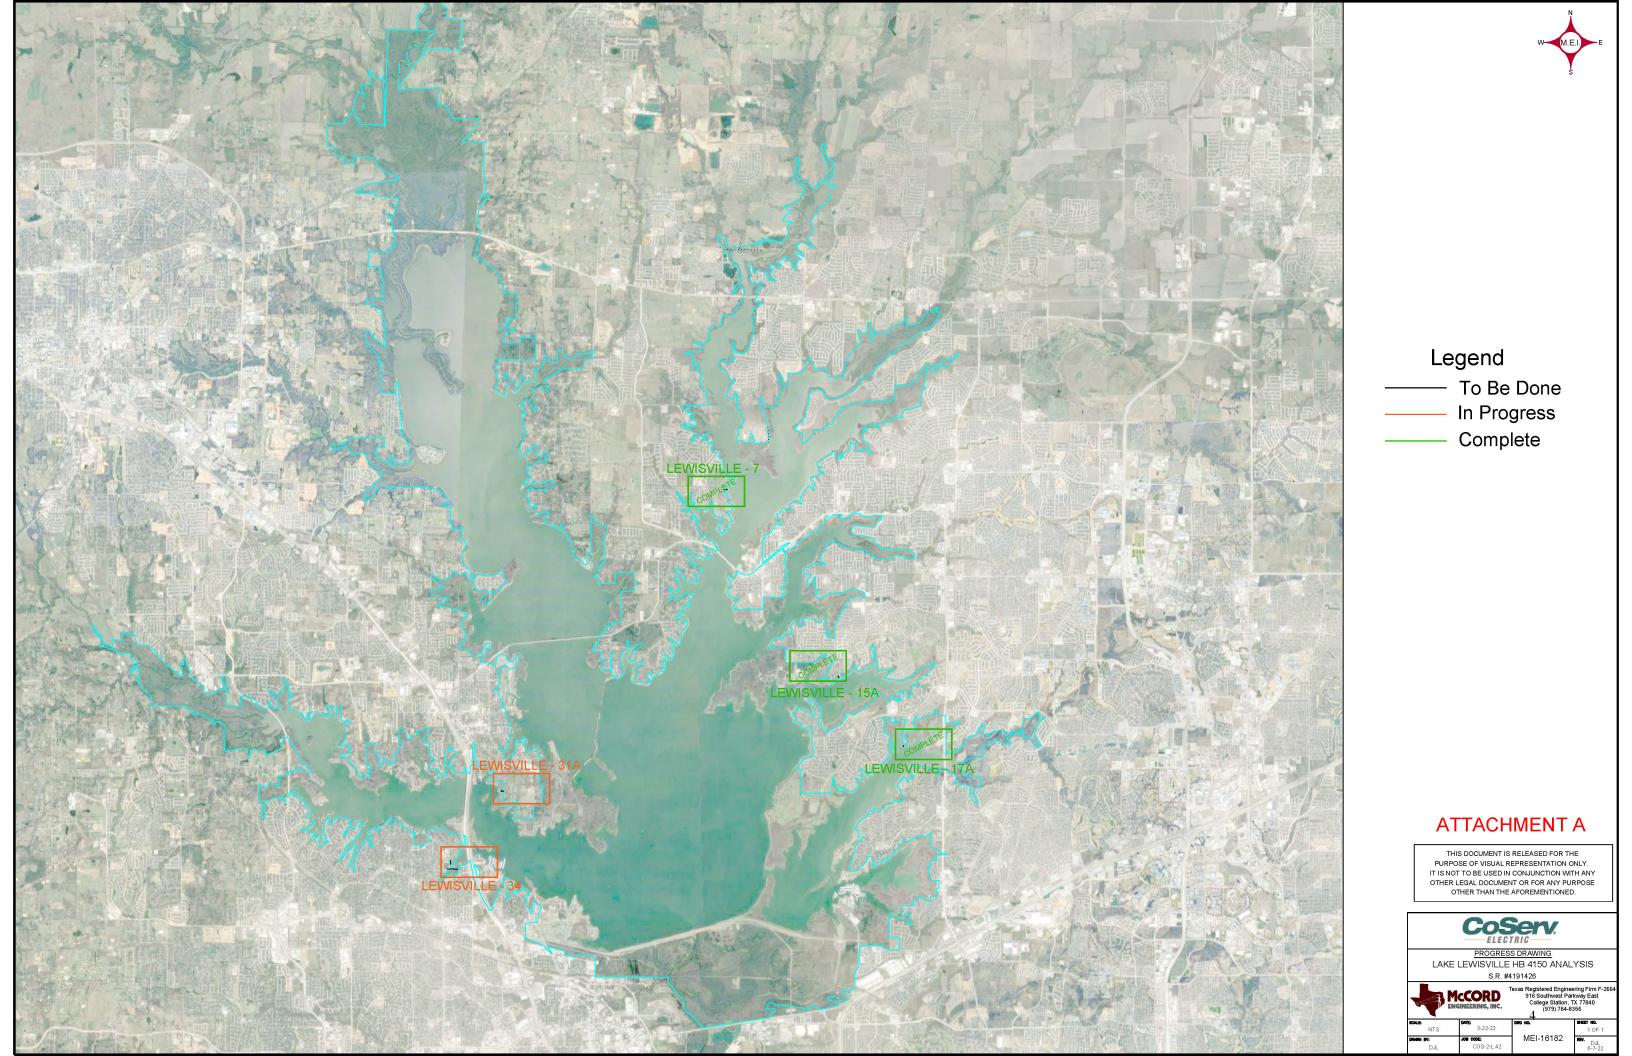

ATTACHMENT B NESC - LAKE RAY ROBERTS CLEARANCES

	New Job Code				Flowage Easement Elevation	Reference Pool Elevation	
Lake Ray Roberts	COS-2-L.43	SR #4191432			645.50'	640.5'	

Lake Ray Roberts Crossing Number	Date Analyzed	ACTION NEEDED	WARNING FLAGS INSTALLED (EST.)	COSERV DESIGN COMPLETE	SURVEY COMPLETE	PERMIT SUBMITTED	PERMIT APPROVED	COSERV CONSTRUCTION COMPLETE	NOTES	SUITABLE / NOT SUITABLE (ENGINEERING FIRM DETERMINATION	CLEARANCE COMPLIANCE	LAKE ACRES AT CROSSING
Ray Roberts 3	11/9/2021	Construction - Waiting on 75' and 80' poles	Complete	Complete	Complete	Complete	Complete		Design and Power Line Revisions Required. Estimated 4 Poles to be Replaced.	SUITABLE FOR SAILBOAT	NO	33233.6
Ray Roberts 9	11/9/2021	None	Complete	6/30/2022	7/8/2022	Complete	Complete		Design and Power Line Revisions Required. Estimated 1 Pole to be Replaced.	SUITABLE FOR SAILBOAT	YES	33233.6
Ray Roberts 10	11/9/2021	None	Complete	Complete	N/A	N/A	N/A		Removed CoServ utilities from Army Corp of Engineers Flowage Easements/Reference Pool.	N/A	YES	33233.6
Ray Roberts 20	11/9/2021	In Construction - material received; estimated 2-3 weeks to complete.	Complete	Complete	Complete	Complete	Complete		Design and Power Line Revisions Required. Estimated 8 Poles to Be Replaced.	SUITABLE FOR SAILBOAT	NO	1929.5

ATTACHMENT B NESC - LAKE LEWISVILLE CLEARANCES ANALYSIS

Flowage Easement Elevation

Reference Pool Elevation

Power Line Revision Required. Ordering 90' Poles 14 to 16 weeks. Estimated 8 Poles to be Replaced.

SUITABLE FOR SAILBOAT

	Lake Lewisville	COS-2-L.42	5K #4191426					537.00	532.00			
Lake Lewisville Crossing Number	Date Analγzed	ACTION NEEDED	WARNING FLAGS INSTALLED (EST.)	COSERV DESIGN COMPLETE	SURVEY COMPLETE	PERMIT SUBMITTED	PERMIT APPROVED	COSERV CONSTRUCTION COMPLETE	NOTES	SUITABLE / NOT SUITABLE (ENGINEERING FIRM DETERMINATION)	CLEARANCE COMPLIANCE	LAKE ACRES AT CROSSING
Lewisville 7	11/5/2021	None	Complete	Complete	N/A	N/A	N/A		Removed CoServ utilities from Army Corp of Engineers Flowage Easement/Reference Pool	SUITABLE FOR SAILBOAT	YES	4609.6
Lewisville 15A	11/5/2021	None	Complete	Complete	N/A	N/A	N/A		Removed CoServ utilities from Army Corp of Engineers Flowage Easement/Reference Pool	SUITABLE FOR SAILBOAT	YES	22291.6
Lewisville 17A	11/5/2021	None	Complete	Complete	N/A	N/A	N/A		Removed CoServ utilities from Army Corp of Engineers Flowage Easement/Reference Pool	SUITABLE FOR SAILBOAT	YES	22291.6
Lewisville 31A	11/5/2021	Engineering Package Preliminary - Electrician installing new Meter Pedestal and underground Service for Member	Complete	9/16/2022	N/A	N/A	N/A		Design to remove CoServ utilities from Army Corp of Engineers Howage Easement/Reference Pool	SUITABLE FOR SAILBOAT	NO	22291.6

Complete

Complete

Construction - Waiting on concrete pole

Complete

11/5/2021
