

Filing Receipt

Filing Date - 2024-07-12 03:06:09 PM

Control Number - 52667

Item Number - 184

PROJECT NO. 52667

§

ş

§

FILING OF ATTESTATIONS DEMONSTRATING COMPLIANCE WITH HB 4150

PUBLIC UTILITY COMMISSION OF TEXAS

PROGRESS REPORT OF DENTON COUNTY ELECTRIC COOPERATIVE, INC., D/B/A <u>COSERV ELECTRIC</u>

Denton County Electric Cooperative, Inc. d/b/a CoServ Electric files this progress report regarding compliance with Section 6 of House Bill 4150 ("HB 4150"), providing information regarding distribution lines on United States Army Corps of Engineers ("USACE") property that CoServ Electric identified as non-compliant in its report and attestation filed in this docket on January 14, 2022 ("Initial Report"). By letter dated March 4, 2022, the Division of Compliance and Enforcement ("DICE") of the Public Utility Commission of Texas ("Commission") requested a progress report and additional information to be filed on a monthly basis. This is CoServ Electric's progress report for July 2024, which is timely filed.

I. Progress Report

In its last progress report, CoServ Electric identified two distribution line segments located in areas that could be suitable for a sailboat and remained non-compliant with the applicable clearance standards in Rule 232 of NESC Standard ANSI (c)(2) ("NESC Rule 232"). These two line segments remain in progress at Lake Lewisville, as described below.

1. Status of engineering design, permitting, and reconstruction.

The status of the remaining distribution line segments is as follows:

 Lewisville 31A – USACE has approved the location of new customer-owned meter pedestal and underground facilities to four existing boathouses and one security light, however the affected CoServ Electric member-customer is still working to obtain easement rights and approvals for the customer-owned facilities. Due to the passage of time, CoServ Electric has coordinated with the member-customer to disconnect CoServ Electric facilities so the overhead facilities can be removed. CoServ Electric estimates that the overhead facilities will be removed before the end of July 2024. Once the member-customer obtains necessary approvals, CoServ Electric will reestablish underground service on the private property. • Lewisville 34 – Redesign for underground facilities completed and submitted to USACE for permit approval. CoServ Electric is still waiting on USACE approval to begin construction. CoServ Electric has had recent contact with USACE to inquire about status and emphasize the need for approval of the revised design. CoServ Electric is hopeful that approval will be obtained before the end of July 2024, and anticipates that, upon approval, construction will take approximately one month.

Further information is provided in Attachments A and B attached hereto.


Date: July 12, 2024

Respectfully submitted,

CPR. CEt

Carl R. Galant State Bar No. 24050633 Travis Vickery State Bar No. 00794790 MCGINNIS LOCHRIDGE LLP 1111 W. 6th Street, Bldg. B, Suite 400 Austin, Texas 78703 Phone: (512) 495-6083 Fax: (512) 505-6383 cgalant@mcginnislaw.com tvickery@mcginnislaw.com

ATTORNEYS FOR COSERV ELECTRIC

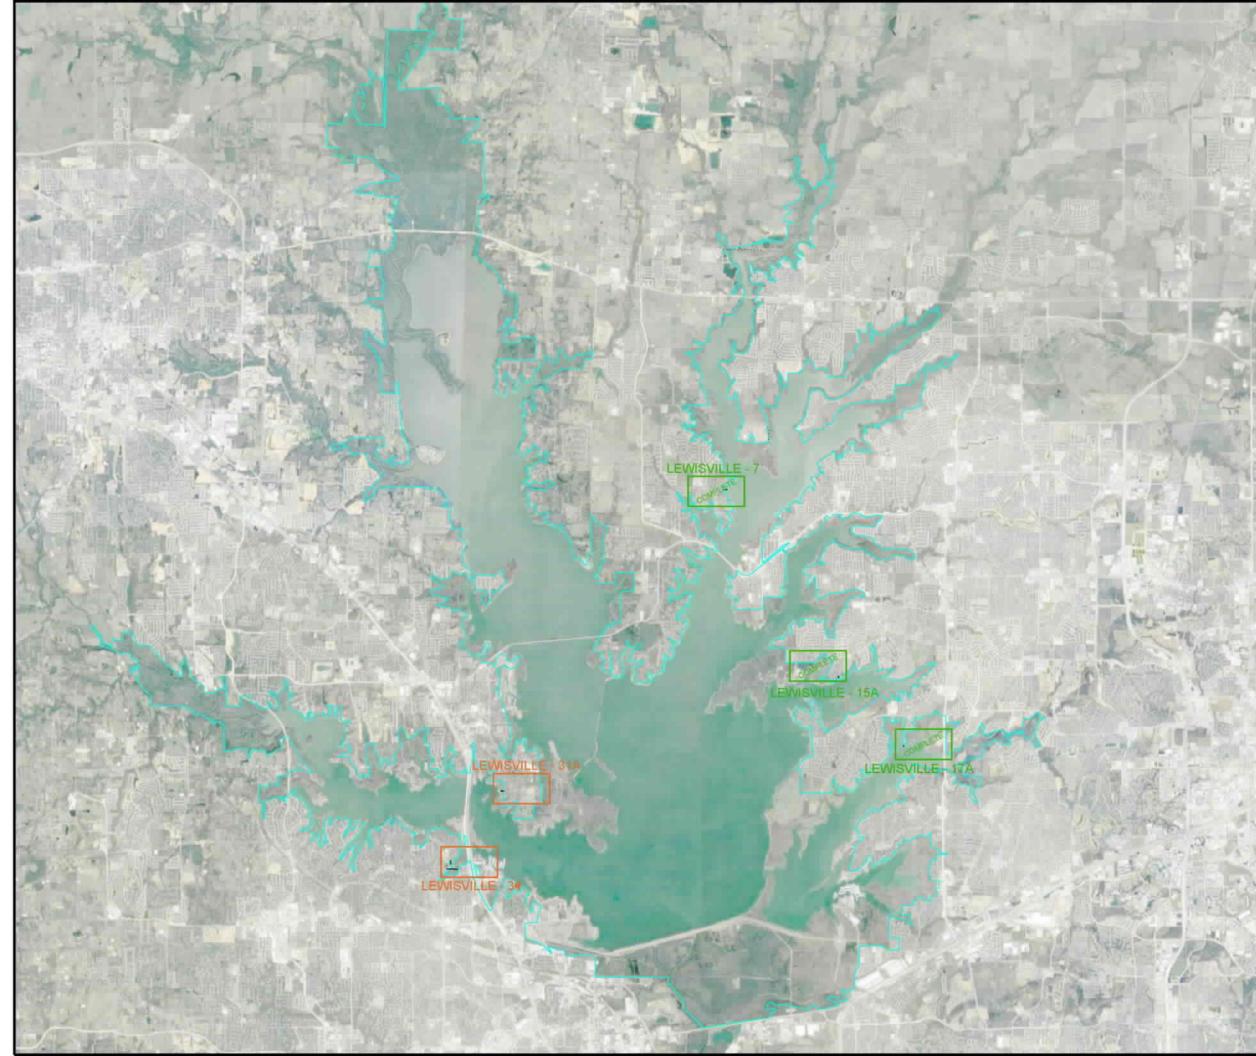

Legend

- To Be Done
- In Progress
- Complete

ATTACHMENT A

THIS DOCUMENT IS RELEASED FOR THE PURPOSE OF VISUAL REPRESENTATION ONLY. IT IS NOT TO BE USED IN CONJUNCTION WITH ANY OTHER LEGAL DOCUMENT OR FOR ANY PURPOSE OTHER THAN THE AFOREMENTIONED.

		Serv	
LA	KE LEWISVILL	ESS DRAWING E HB 4150 ANAL #4191426	YSIS
-	MCCORD ENGINEERING, INC.	Texas Registered Engine 916 Southwest Pa	riterity East
NAR HIS	5-23-22 All 1006 CO16-24 42	MEI-16182	10F1

ATTACHMENT & NESC - LAKE LEWISVILLE CLEARANCES ANALYSIS

	New Job Code		xde				Flowinge Ensement Elevation		Reference Pool Elevation			
	Lake Lewisville	005-2-1.42	58.#4191425					\$37.00	532.00']		
Lake Lewisville Crossing Number	Date Analyzed	ACTION NEEDED	WARNING FLAGS INSTALLED (EST.)	COSERV DESIGN COMPLETE	SURVEY	PERMIT SUBMITTED	PERMIT	COSERV CONSTRUCTION COMPLETE	NOTES	SUITABLE / NOT SUITABLE (ENGINEERING FIRM DETERMINATION)	CLEARANCE	LAKE ACRES AT CROSSING
tenisille 7	11/5/2025	None	Complete	Complete	N/A.	N/A	N/A		Removed Cadery utilities from Army Corp of Engineers Howage Lasement/Reference Pool	SUITABLE FOR SALBOAT	.115	4608.6
Levraville 15A	13/5/2021	Morre	Complete	Complete	N/A	N/A	N/A	Complete	Removed CoServ utilities from Army Corp of Engineers Howage Lasmoent/Reference Pool	SUITABLE FOR SALBOAT	785	22291.6
Let wind willie 17A	11/5/2021	None	Complete	Complete	N/A	N/A	N/A	Compilete	Removed CaServ utilities from Army Cocp of Engineers Elemage Casement/Reference Fool	SUITABLE FOR SALDOAT	383	22291.0
Level willie 33.0	11/9/2021	Engineering Package Preliminary - Clectrician Installing new Meter Pedestal and underground Service for Member	Complete	9/16/2022	N/A	N/A	N/A		Design to remove Cablev utilities from Army Carp of Engineers Resage Lasement/Reference Pool	SUITABLE FOR SAUBOAT	(mp)	22291.6
tenisille 34	11/5/2021	Approval from USACE for Revised Overhead and Underground Design	Complete	Complete	Complete	Complete	USALI to review Revisions		Power Line Revision Required. To Resolve issue's with NY Concrete Poles and moset Regulatory Compliance we are converting a section of Overhead to Underground.	MITABLE FOR SAILBOAT	NO	22291.6
