

Filing Receipt

Filing Date - 2024-09-11 12:37:31 PM

Control Number - 52667

Item Number - 188

PROJECT NO. 52667

FILING OF ATTESTATIONS	§	PUBLIC UTILITY COMMISSION
DEMONSTRATING COMPLIANCE	§	
WITH HB 4150	§	OF TEXAS

PROGRESS REPORT OF DENTON COUNTY ELECTRIC COOPERATIVE, INC., D/B/A COSERV ELECTRIC

Denton County Electric Cooperative, Inc. d/b/a CoServ Electric files this progress report regarding compliance with Section 6 of House Bill 4150 ("HB 4150"), providing information regarding distribution lines on United States Army Corps of Engineers ("USACE") property that CoServ Electric identified as non-compliant in its report and attestation filed in this docket on January 14, 2022 ("Initial Report"). By letter dated March 4, 2022, the Division of Compliance and Enforcement ("DICE") of the Public Utility Commission of Texas ("Commission") requested a progress report and additional information to be filed on a monthly basis. This is CoServ Electric's progress report for September 2024, which is timely filed.

I. Progress Report

In its last progress report, CoServ Electric identified two distribution line segments located in areas that could be suitable for a sailboat and remained non-compliant with the applicable clearance standards in Rule 232 of NESC Standard ANSI (c)(2) ("NESC Rule 232"). Only one line segment remains in progress at Lake Lewisville, as described below. CoServ Electric completed the construction of Lewisville 31A, which is now compliant with the applicable clearance standards.

1. Status of engineering design, permitting, and reconstruction.

The status of the remaining distribution line segment is as follows:

 Lewisville 34 – Redesign for underground facilities completed and submitted to USACE for permit approval. CoServ Electric is still waiting on USACE approval to begin construction. Although CoServ Electric met with USACE to discuss status and emphasize the need for approval of the revised design after the July 2024 progress report, that approval has not yet been received. Upon approval, CoServ Electric expects construction will take approximately one month.

Further information is provided in Attachments A and B attached hereto.

Date: September 11, 2024 Respectfully submitted,

Carl R. Galant

State Bar No. 24050633

Travis Vickery

State Bar No. 00794790

MCGINNIS LOCHRIDGE LLP
1111 W. 6th Street, Bldg. B, Suite 400

OR. Cet

Austin, Texas 78703


Phone: (512) 495-6083

Fax: (512) 505-6383

cgalant@mcginnislaw.com

tvickery@mcginnislaw.com

ATTORNEYS FOR COSERV ELECTRIC

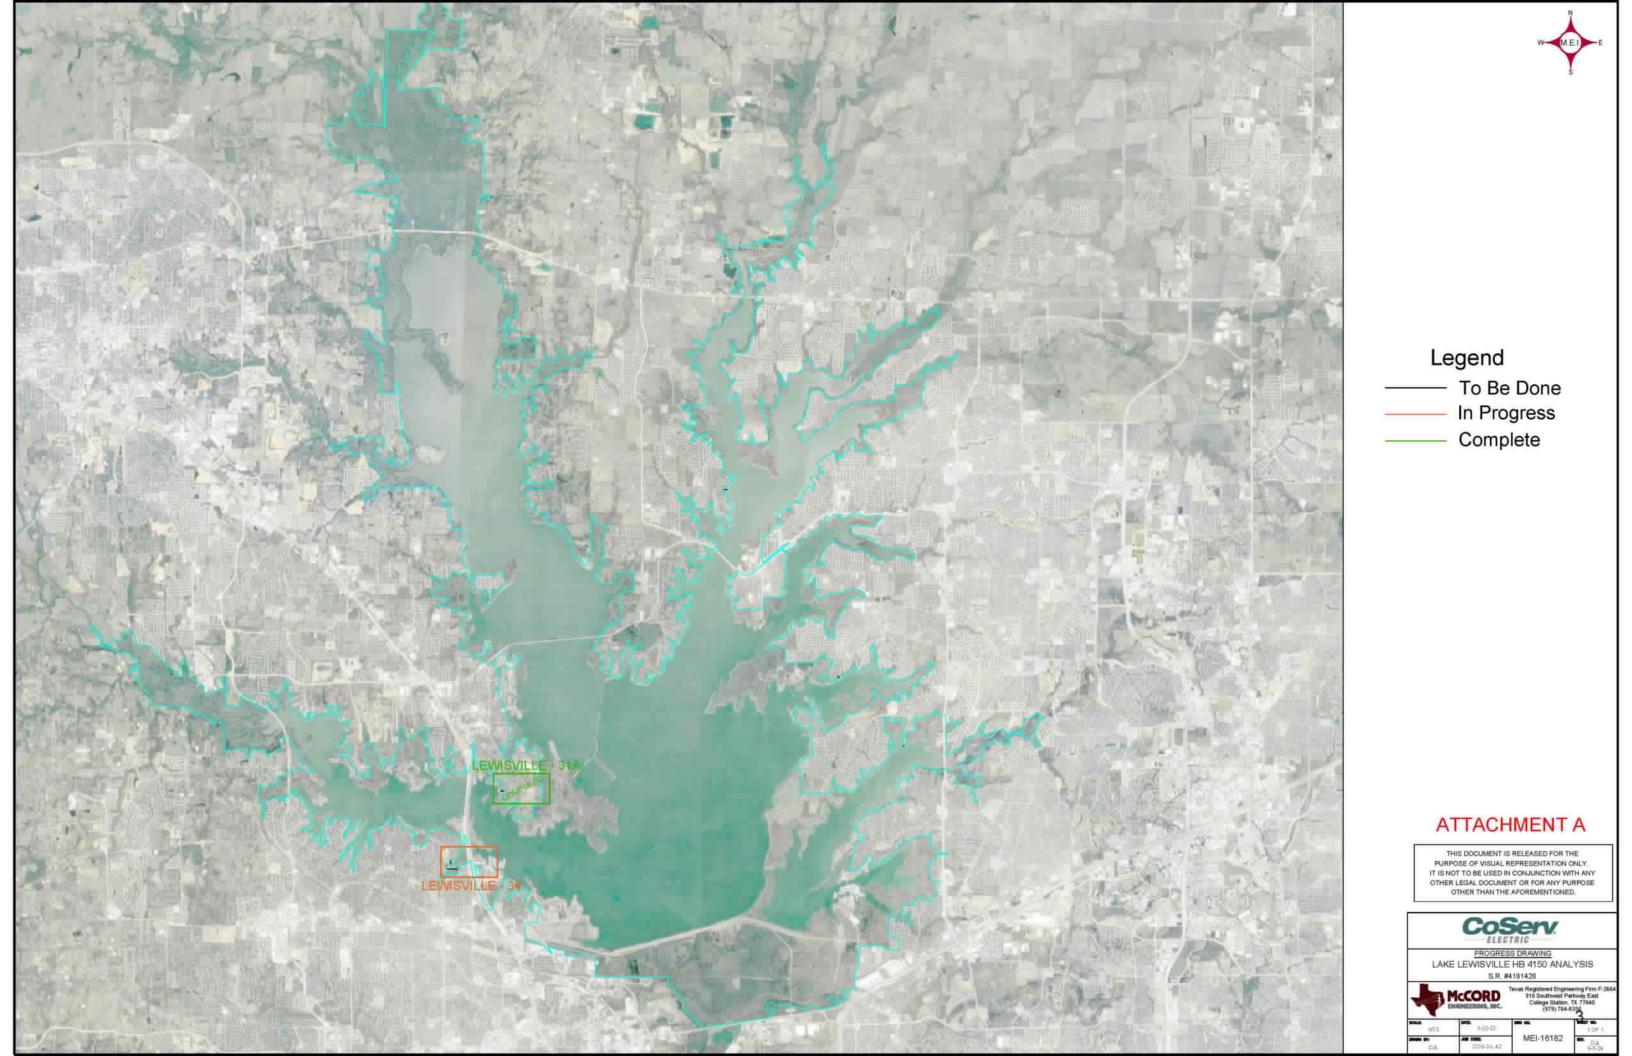

ATTACHMENT B NESC - LAKE LEWISVILLE CLEARANCES ANALYSIS

		New Job Code			Flowage Easement Elevati		ment Elevation	Reference Pool Elevation				
	Lake Lewisville	COS-2-L42	SR m4191426					537.00	532.00			
Lake Lewisville Crossing Number	Darte Analyzed	ACTION NEEDED	WARNING FLAGS INSTALLED (EST.)	COSERV DESIGN COMPLETE	SURVEY COMPLETE	PERMIT SUBMITTED	PERMIT APPROVED	COSERV CONSTRUCTION COMPLETE	NOTES	SUITABLE / NOT SUITABLE (ENGINEERING FIRM DETERMINATION)	CLEARANCE COMPLIANCE	LAKE ACRES AT CROSSING
Lewi sville 31A	11/5/2021	Engineering Package Preliminary - Electrician installing new Meter Pedestal and underground Service for Member	Complete	Complete	N/A	N/A	N/A		Ranaved CoServ utilities from Army Carp of Engineers Flavouge Eusement/Belerem e Pool	SHITABIT FOR SAHRDAT	Yes	22291.6
Lewisville 34	11/6/2021	Approval from USACE for Revised Overhead and Underground Design	Complete	Complete	Complete	Complete	USACE to review Regisions		Power Line Revision Required. To Resolve issues with 90' Compete Poles and meet Regulatory Compliance we are converting a section of Overhead to	SHITABLE FOR SAHDOAT	NO	22291.6
