

Filing Receipt

Received - 2022-08-10 09:53:30 AM Control Number - 52667 ItemNumber - 86

PROJECT NO. 52667

FILING OF ATTESTATIONS	§	PUBLIC UTILITY COMMISSION
DEMONSTRATING COMPLIANCE	§	
WITH HB 4150	§	OF TEXAS

SIXTH PROGRESS REPORT OF DENTON COUNTY ELECTRIC COOPERATIVE, INC., D/B/A COSERV ELECTRIC

Denton County Electric Cooperative, Inc d/b/a CoServ Electric files this progress report regarding compliance with Section 6 of House Bill 4150 ("HB 4150"), providing information regarding distribution lines on United States Army Corps of Engineers ("USACE") property that CoServ Electric identified as non-compliant in its report and attestation filed in this docket on January 14, 2022 ("Initial Report"). By letter dated March 4, 2022, the Division of Compliance and Enforcement ("DICE") of the Public Utility Commission of Texas ("Commission") requested a progress report and additional information to be filed on a monthly basis. This is CoServ Electric's sixth monthly progress report, which is timely filed.

I. Sixth Progress Report

In its last progress report, CoServ Electric identified five distribution line segments located in areas that could be suitable for a sailboat and remained non-compliant with the applicable clearance standards in Rule 232 of NESC Standard ANSI (c)(2) ("NESC Rule 232"). These five line segments remain in progress at Lake Ray Roberts or Lake Lewisville, as described below.

1. Status of engineering design, permitting, and reconstruction.

The status of the five remaining distribution line segments is as follows:

- Ray Roberts 3 In construction; waiting for delivery of 75-foot and 80-foot wood poles.
- Ray Roberts 9 Survey completed based on redesign of layout; permit submitted and approved; CoServ Electric is now working with USACE to gain access to the site, which requires adding a gate and tree removal in heavily wooded area.
- Ray Roberts 20 Waiting on approval of permit submitted June 24, 2022.
- Lewisville 31A Design and easement acquisition still in progress based on discussions with USACE and private landowner. The current proposal involves removal of CoServ Electric's overhead facilities from USACE property and installation

of new underground service to four existing boathouses and a security light. CoServ is coordinating with an electrician regarding relocation of the landowner's electric service.

• Lewisville 34 – Permit approved; waiting for delivery of 90-foot concrete pole to begin construction.

Further information is provided in Attachments A and B attached hereto.

Date: August 10, 2022 Respectfully submitted,

Carl R. Galant

State Bar No. 24050633

Travis Vickery

State Bar No. 00794790

1111 W. 6th Street, Bldg. B, Suite 400

CPR. Cet


Austin, Texas 78703


Phone: (512) 495-6083 Fax: (512) 505-6383

cgalant@mcginnislaw.com

tvickery@mcginnislaw.com

ATTORNEYS FOR COSERV ELECTRIC

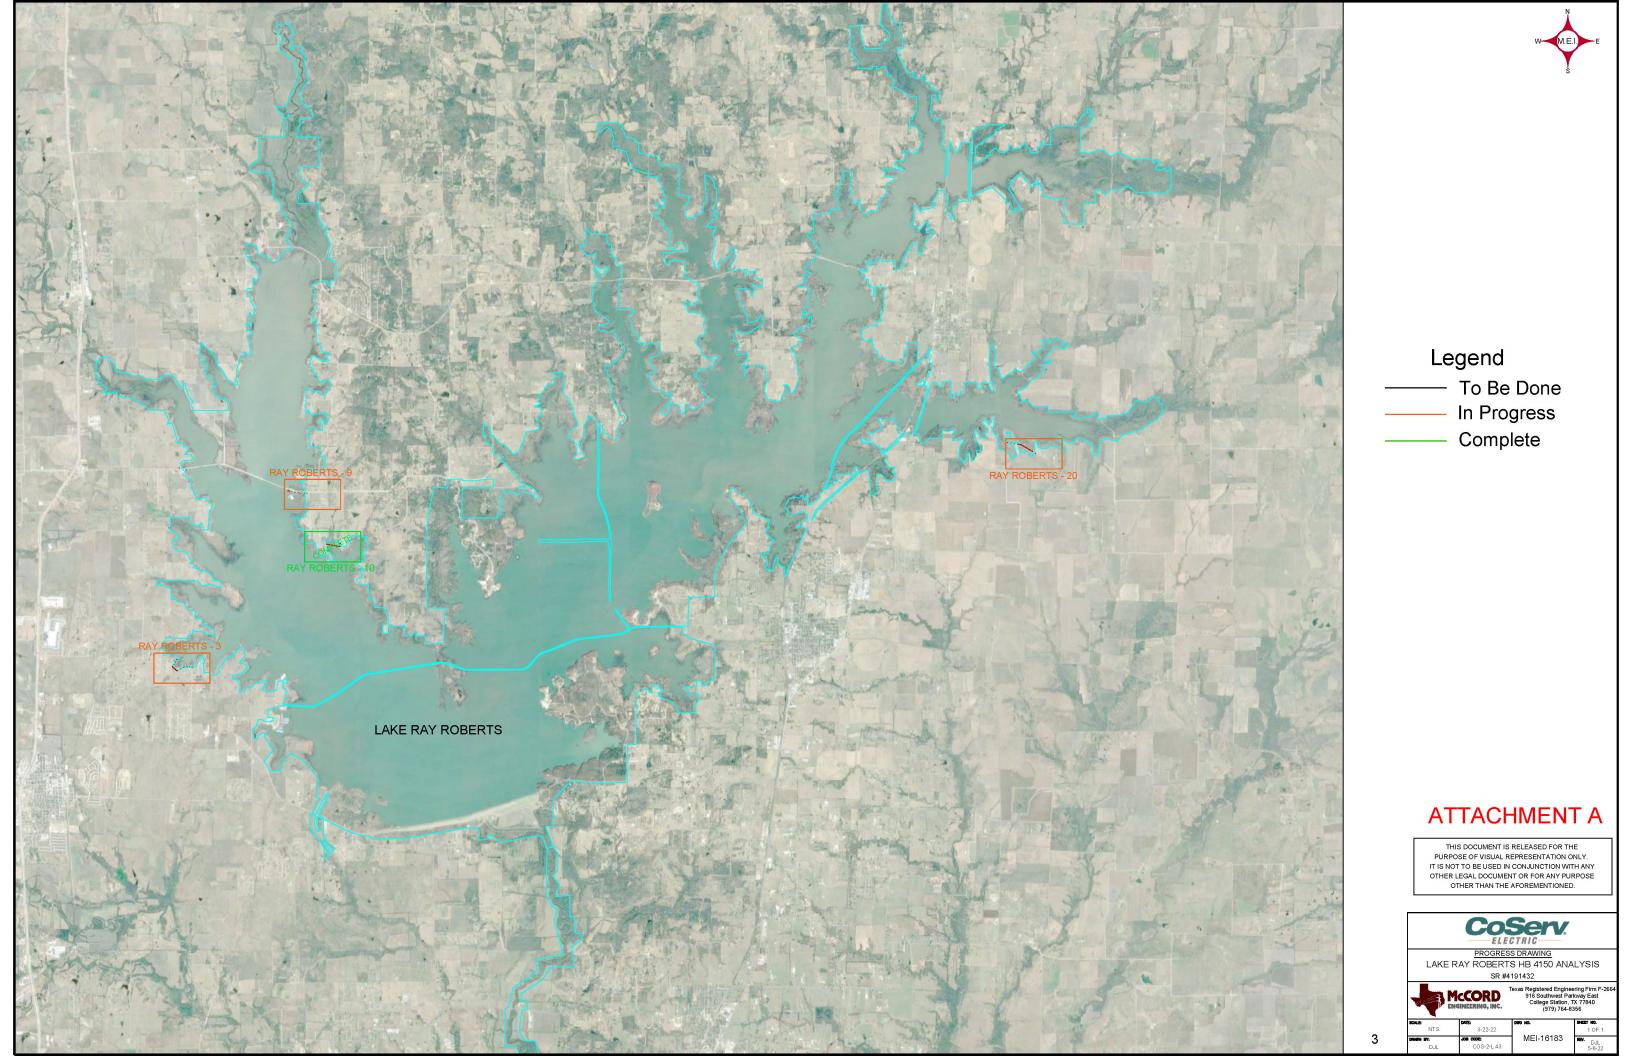

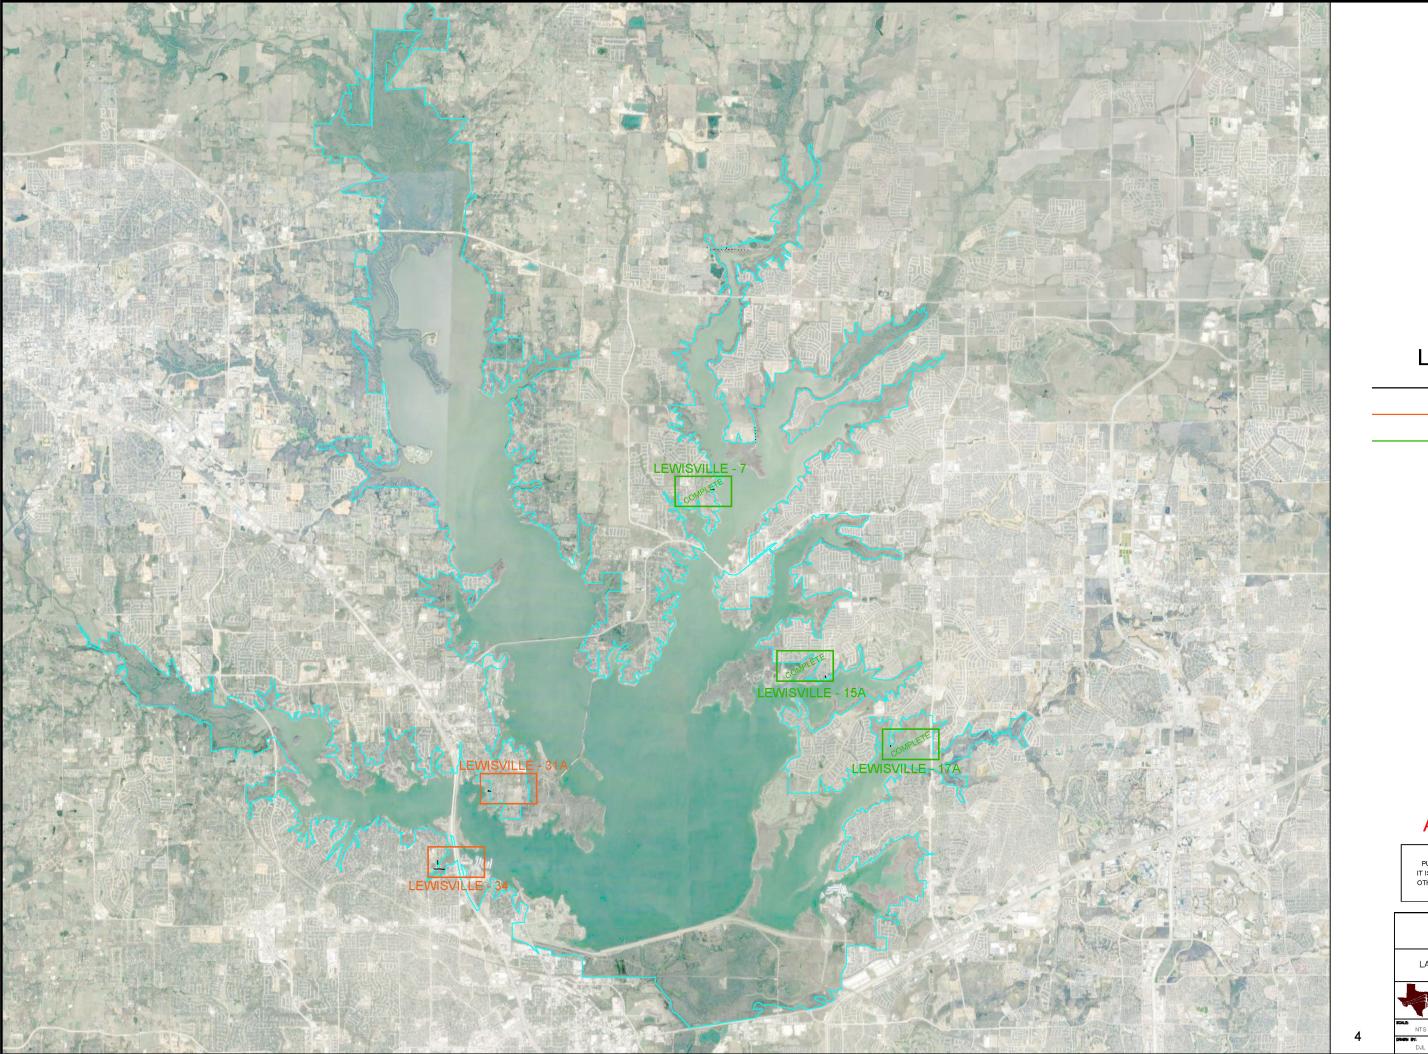



Legend

- To Be Done In Progress Complete

ATTACHMENT A

THIS DOCUMENT IS RELEASED FOR THE PURPOSE OF VISUAL REPRESENTATION ONLY. IT IS NOT TO BE USED IN CONJUNCTION WITH ANY OTHER LEGAL DOCUMENT OR FOR ANY PURPOSE OTHER THAN THE AFOREMENTIONED.



PROGRESS DRAWING LAKE LEWISVILLE HB 4150 ANALYSIS S.R. #4191426



ATTACHMENT B NESC - LAKE RAY ROBERTS CLEARANCES

		New Job Co	ode				Flowage Easement Elevation		Reference Pool Elevation			
	Lake Ray Roberts	COS-2-L.43	SR #4191432				64	5.50'	640.5'			
Lake Ray Roberts Crossing Number	Date Analyzed	ACTION NEEDED	WARNING FLAGS INSTALLED (EST.)	COSERV DESIGN COMPLETE	SURVEY COMPLETE	PERMIT SUBMITTED	PERMIT APPROVED	COSERV CONSTRUCTION COMPLETE	NOTES	SUITABLE / NOT SUITABLE (ENGINEERING FIRM DETERMINATION	CLEARANCE COMPLIANCE	LAKE ACRES AT CROSSING
Ray Roberts 3	11/9/2021	Construction - Waiting on 75' and 80' poles	Complete	Complete	Complete	Complete	Complete		Design and Power Line Revisions Required. Estimated 4 Poles to be Replaced.	SUITABLE FOR SAILBOAT	NO	33233.6
Ray Roberts 9	11/9/2021	Construction - Working with Corp of Enineers on access to site	Complete	6/30/2022	7/8/2022	Complete	Complete	9/2/2022	Design and Power Line Revisions Required. Estimated 1 Pole to be Replaced.	SUITABLE FOR SAILBOAT	NO	33233.6
Ray Roberts 10	11/9/2021	None	Complete	Complete	N/A	N/A	N/A		Removed CoServ utilities from Army Corp of Engineers Flowage Easements/Reference Pool.	N/A	YES	33233.6
Ray Roberts 20	11/9/2021	Permit	Complete	Complete	Complete	6/24/2022			Design and Power Line Revisions Required. Estimated 8 Poles to Be Replaced.	SUITABLE FOR SAILBOAT	NO	1929.5

ATTACHMENT B NESC - LAKE LEWISVILLE CLEARANCES ANALYSIS

								ř				
		New Job Code					Flowage Easement Elevation		Reference Pool Elevation			
	Lake Lewisville	COS-2-L.42	SR #4191426					537.00'	532.00'			
Lake Lewisville Crossing Number	Date Analyzed	ACTION NEEDED	WARNING FLAGS INSTALLED (EST.)	COSERV DESIGN COMPLETE	SURVEY COMPLETE	PERMIT SUBMITTED	PERMIT APPROVED	COSERV CONSTRUCTION COMPLETE	NOTES	SUITABLE / NOT SUITABLE (ENGINEERING FIRM DETERMINATION)	CLEARANCE COMPLIANCE	LAKE ACRES AT CROSSING
Lewisville 7	11/5/2021	None	Complete	Complete	N/A	N/A	N/A		Removed CoServ utilities from Army Corp of Engineers Flowage Easement/Reference Pool	SUITABLE FOR SAILBOAT	YES	4609.6
Lewisville 15A	11/5/2021	None	Complete	Complete	N/A	N/A	N/A	Complete	Removed CoServ utilities from Army Corp of Engineers Flowage Easement/Reference Pool	SUITABLE FOR SAILBOAT	YES	22291.6
Lewi sville 17A	11/5/2021	None	Complete	Complete	N/A	N/A	N/A		Removed CoServ utilities from Army Corp of Engineers Flowage Easement/Reference Pool	SUITABLE FOR SAILBOAT	YES	22291.6
Lewisville 31A	11/5/2021	Need New Engineering Package - Working with electrician on relocating Member's services	Complete	8/26/2022					Design and Power Line Revisions Required. Estimated 4 Poles to be Replaced.	SUITABLE FOR SAILBOAT	NO	22291.6
Lewisville 34	11/5/2021	Construction - Waiting on concrete pole	Complete	Complete	Complete	Complete	Complete		Power Line Revision Required. Ordering 90' Poles 14 to 16 weeks. Estimated 8 Poles to be Replaced.	SUITABLE FOR SAILBOAT	NO	22291.6
